LANDAU ASSOCIATES

TECHNICAL MEMORANDUM

TO: Amy Young

FROM: Katie Gauglitz, LG

DATE: May 1, 2026

RE: **Well Decommissioning**
Webster Nursery
Tumwater, Washington
Project No. 774006.040.048

INTRODUCTION

This technical memorandum summarizes well decommissioning activities completed by Landau Associates, Inc. (Landau) at the Washington State Department of Natural Resources (DNR) Webster Nursery site, a former pesticide-storage warehouse in Tumwater, Washington (Site; Figure 1). The Site is associated with past releases of organochlorine pesticides to soil and groundwater. Constituents of concern included the organochlorine pesticides heptachlor epoxide (HE; breakdown product of heptachlor) and chlordanes.

Remedial action excavation and disposal of HE-contaminated soil was completed in August 2018 and a summary of the remedial action was provided in a Cleanup Action Completion Report (Landau 2020). The Washington State Department of Ecology (Ecology) approved the Compliance Monitoring Plan and finalized the plan on April 14, 2023 (Landau 2023). Additional soil sampling was completed in 2024 in accordance with the sub-slab soil investigation work plan (Landau 2024) to confirm clean conditions for soil beneath the warehouse.

Per the Agreed Order, DNR requested Ecology 1) evaluate the overall success of the cleanup, 2) issue a letter indicating the confirmational monitoring requirements were satisfied, and 3) provide concurrence that cleanup is complete. Ecology issued a No Further Action determination letter for the Site on December 19, 2025 stating that the cleanup has been satisfactorily completed (Ecology 2025).

MONITORING WELL DECOMMISSIONING

All groundwater monitoring wells associated with the remedial action (SW-1, SW-9R, SW-10R, SW-11R, SW-12, SW-13, SW-14, SW-15, and SW-16) were decommissioned by Holt Services, Inc. on March 18th, 2026 in accordance with WAC 173-160-381(1)(a)(iii). A utility locate was completed prior to the well decommissioning activities. Each well was decommissioned by placing 3/8-inch bentonite chips inside the well casing from the bottom of the well to 1 foot (ft) below ground surface (bgs); where, the remaining 1 foot to ground surface was completed with neat cement. Well monuments and/or bollards

were removed from each well location, except at MW-12 where the flush-mount well monument was left in place. Well decommissioning details are summarized in the table below:

Site Well ID	Ecology Well ID	Bentonite Chips (ft bgs)	Neat Cement (ft bgs)
SW-1	ABY892	1-20	0-1
SW-9R	BKR472	1-16	0-1
SW-10R	BKR473	1-16	0-1
SW-11R	BKR474	1-16	0-1
SW-12	ACN087	1-15	0-1
SW-13	AEM471	1-20	0-1
SW-14	AEM472	1-20	0-1
SW-15	AEM473	1-20	0-1
SW-16	AEM474	1-20	0-1

Monitoring well locations are shown on Figure 2. Well decommissioning logs are in provided in Appendix A.

USE OF THIS REPORT

This technical memorandum has been prepared for the exclusive use of Washington State Department of Natural Resources and Washington State Department of Ecology for specific application to the Webster Nursery Site. No other party is entitled to rely on the information, conclusions, and recommendations included in this document without the express written consent of Landau Associates. Further, the reuse of information, conclusions, and recommendations provided herein for extensions of the project or for any other project, without review and authorization by Landau Associates, shall be at the user's sole risk. Landau Associates warrants that within the limitations of scope, schedule, and budget, our services have been provided in a manner consistent with that level of care and skill ordinarily exercised by members of the profession currently practicing in the same locality under similar conditions as this project. Landau Associates makes no other warranty, either express or implied.

This document has been prepared under the supervision and direction of the following key staff.

LANDAU ASSOCIATES, INC.

Katie M. Gauglitz

Katie Gauglitz, LG
Associate Geologist

JDB/KMG/tmh
[Y:\774\006 WEBSTER\R\WELL DECOMMISSIONING\WELL DECOMMISSIONING 2026.DOCX]

Attachments:
Figure 1. Vicinity Map
Figure 2. Monitoring Well Network
Attachment 1. Well Decommissioning Logs

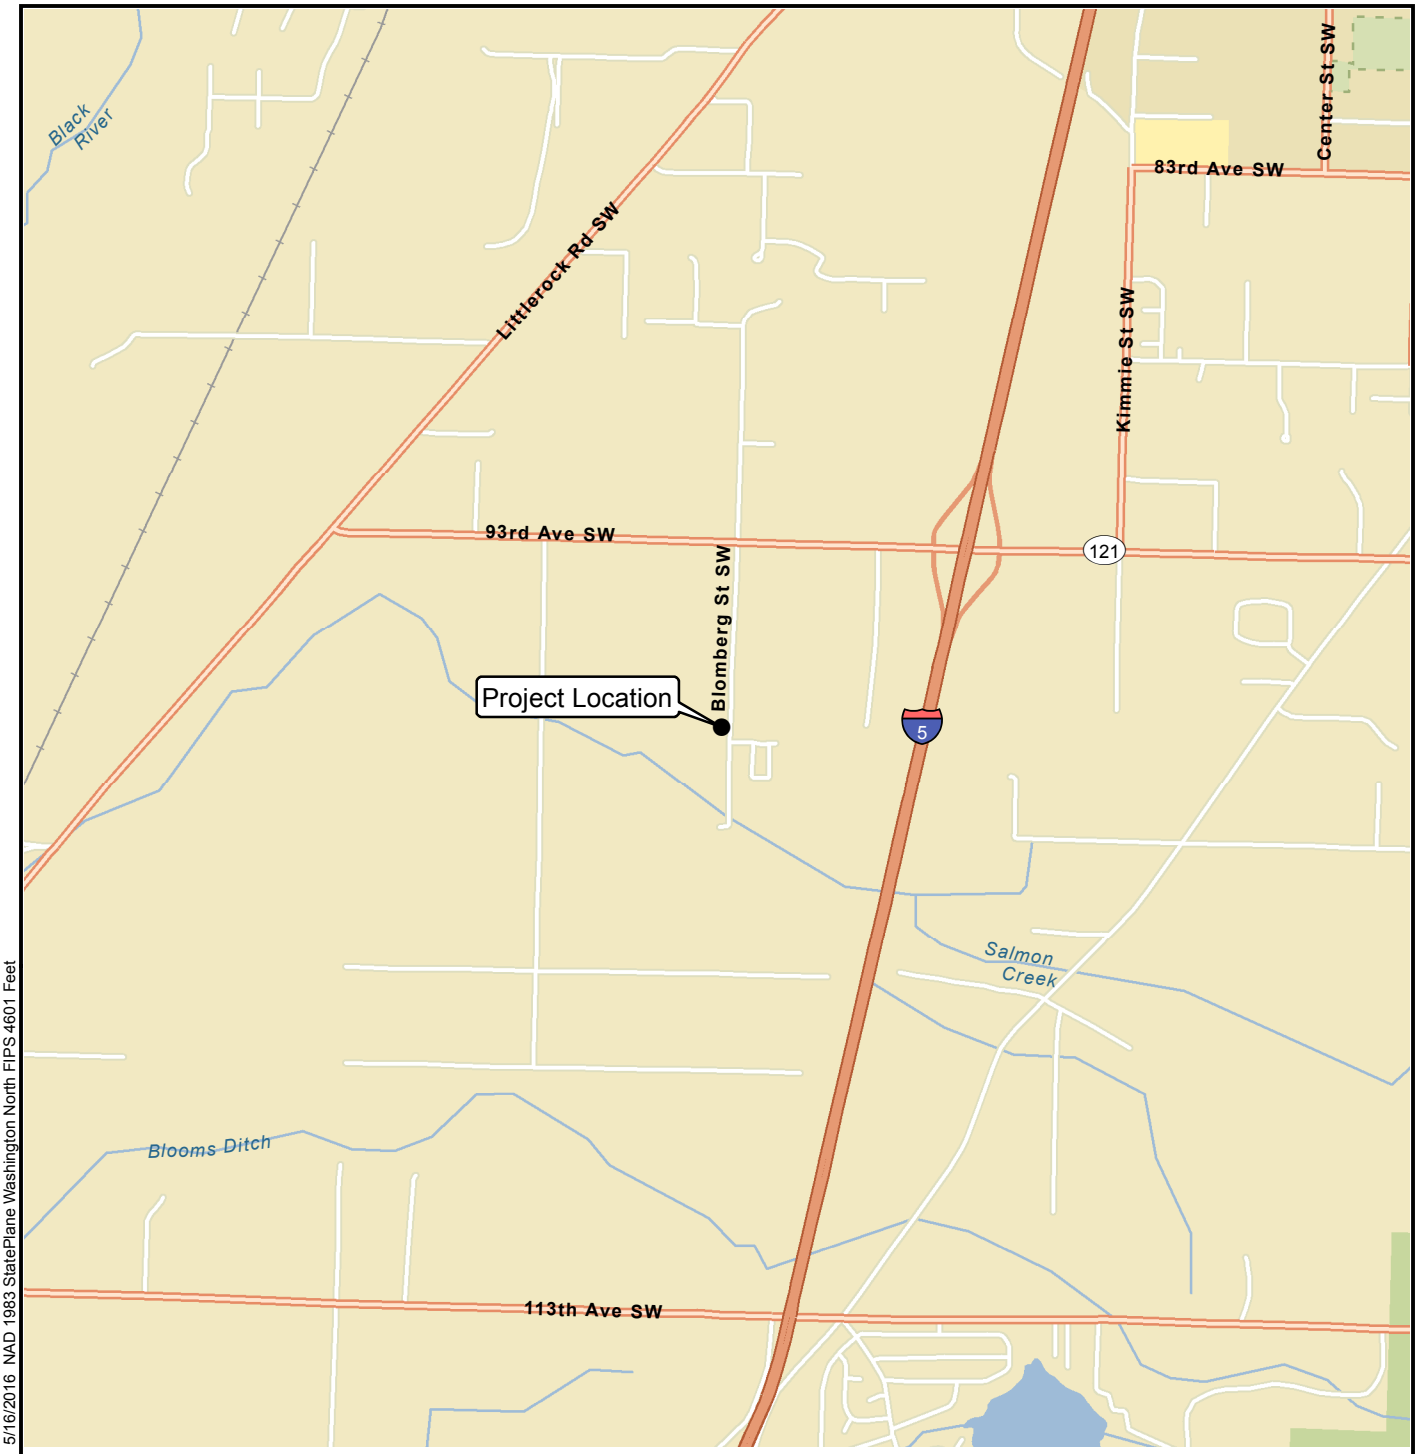
REFERENCES

Ecology. 2025. Letter RE: Status of Agreed Order No. DE 13181 and No Further Action to Complete Cleanup of the following Contaminated Site: Site name: WA DNR Webster Nursery. Site address: 9805 Blomberg St. SW, Tumwater, Thurston County, WA 98512. Cleanup Site ID: 3380. Facility/Site ID: 8786341. Washington State Department of Ecology. December 19.

Landau. 2020. Cleanup Action Completion Report. Washington State Department of Natural Resources. Webster Nursery. Tumwater, Washington. Prepared for Washington State Department of Natural Resources. P.O. Box 47030. Olympia, Washington. May 29.

Landau. 2023. Technical Memorandum RE: Compliance Monitoring Plan, Webster Nursery Site, Site Identification 3380, Tumwater, Washington. Landau Project No. 0774006.040.047. Landau Associates, Inc.

Landau. 2024. Sub-Slab Soil Investigation Work Plan. Webster Nursery, 9805 Blomberg Street Tumwater, Washington. Prepared for Washington State Department of Natural Resources, PO Box 47030, Olympia, Washington. April 4.



N

0 0.5 1

Miles



Data Source: Esri 2012

G:\Projects\774\006\020\026\FSIF01 VicinityMap.mxd 5/16/2016 NAD 1983 StatePlane Washington North FIPS 4601 Feet

LANDAU ASSOCIATES

Webster Nursery Site Tumwater, Washington	**Vicinity Map**	Figure 1



Legend

- Monitoring Well
- Tax Parcels

0 50 100

Scale in Feet

Notes

1. SW-9R, SW-10R, and SW-11R are new (replacement) wells.
2. Black and white reproduction of this color original may reduce its effectiveness and lead to incorrect interpretation.

Data Sources: Thurston County GIS; WA DNR Survey, 2018.

G:\Projects\774\006\WebsterNursery\WebsterNursery.aprx 4/30/2026

LANDAU ASSOCIATES

Webster Nursery Site Tumwater, Washington	**Monitoring Well Network**	Figure 2

ATTACHMENT 1

Well Decommissioning Logs

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Type of Work:

☐ Construction
☑ Decommission ⇨ Original NOI No. 205445

Ecology Well ID Tag No. ABY892
Site Well Name SW-1
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for? _____

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature Cody H
License No. 3269
Company Name Holt Services Inc

If trainee box is checked, sponsor's license number: _____
Sponsor's signature _____

Notice of Intent No. AE91507

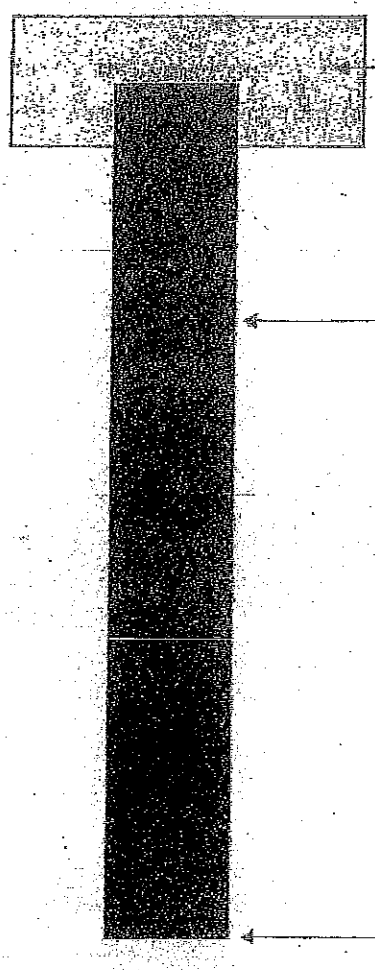
Type of Well:

☑ Resource Protection Well ☐ Injection Point
☐ Remediation Well ☐ Grounding Well
☐ Geotechnical Soil Boring ☐ Ground Source Heat Pump
☐ Environmental Boring ☐ Other _____
↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.948537
Longitude (Example: -120.12345) -122.951514
(WGS 84 Coordinate System)

Borehole diameter _____ inches Casing diameter 2" inches
Static water level _____ ft below top of casing Date _____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing _____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-20' FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 20' FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Notice of Intent No. AE91507

Type of Work:
- ☐ Construction
- ☑ Decommission ⇨ Original NOI No. RE16353

Ecology Well ID Tag No. BKR472
Site Well Name SW-9R
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for?

Type of Well:
- ☑ Resource Protection Well
- ☐ Remediation Well
- ☐ Geotechnical Soil Boring
- ☐ Environmental Boring
- ☐ Injection Point
- ☐ Grounding Well
- ☐ Ground Source Heat Pump
- ☐ Other
- ↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

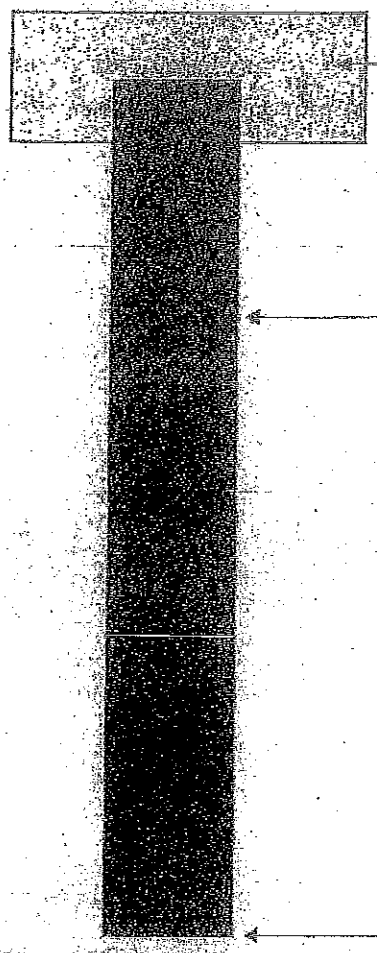
Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature Cody H
License No. 3269
Company Name Holt Services Inc
If trainee box is checked, sponsor's license number:
Sponsor's signature

Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.945725
Longitude (Example: -120.12345) -122.950773
(WGS 84 Coordinate System)

Borehole diameter ____ inches Casing diameter 2" inches
Static water level ____ ft below top of casing Date ____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing ____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-16' FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 16' FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Notice of Intent No. AE91507

Type of Work:
- ☐ Construction
- ☑ Decommission ⇨ Original NOI No. RE16353

Ecology Well ID Tag No. BKR473
Site Well Name SW-10R
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for?

Type of Well:
- ☑ Resource Protection Well
- ☐ Remediation Well
- ☐ Geotechnical Soil Boring
- ☐ Environmental Boring
- ☐ Injection Point
- ☐ Grounding Well
- ☐ Ground Source Heat Pump
- ☐ Other
- ↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

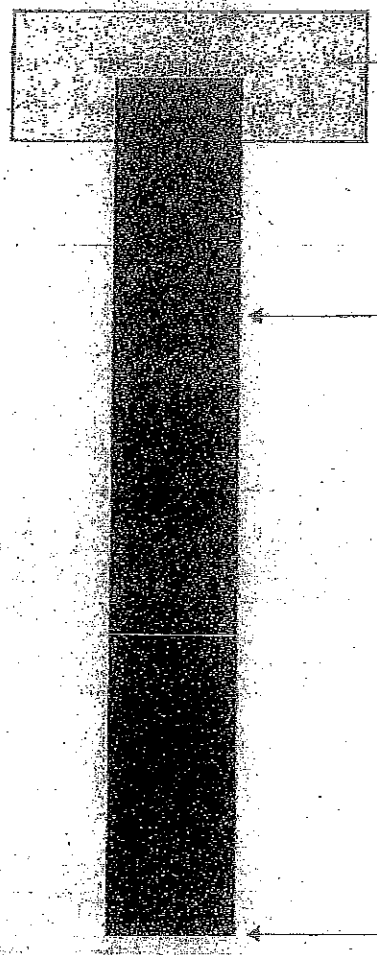
WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature Cody H
License No. 3269
Company Name Holt Services Inc

If trainee box is checked, sponsor's license number:
Sponsor's signature

Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.945588
Longitude (Example: -120.12345) -122.950649
(WGS 84 Coordinate System)

Borehole diameter ____ inches Casing diameter 2" inches
Static water level ____ ft below top of casing Date ____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing ____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-16 FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 16' FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Notice of Intent No. AE91507

Type of Work:
- ☐ Construction
- ☑ Decommission ⇨ Original NOI No. RE16353

Ecology Well ID Tag No. BKR474
Site Well Name SW-11R
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for?

Type of Well:
- ☑ Resource Protection Well
- ☐ Remediation Well
- ☐ Geotechnical Soil Boring
- ☐ Environmental Boring
- ☐ Injection Point
- ☐ Grounding Well
- ☐ Ground Source Heat Pump
- ☐ Other
- ↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

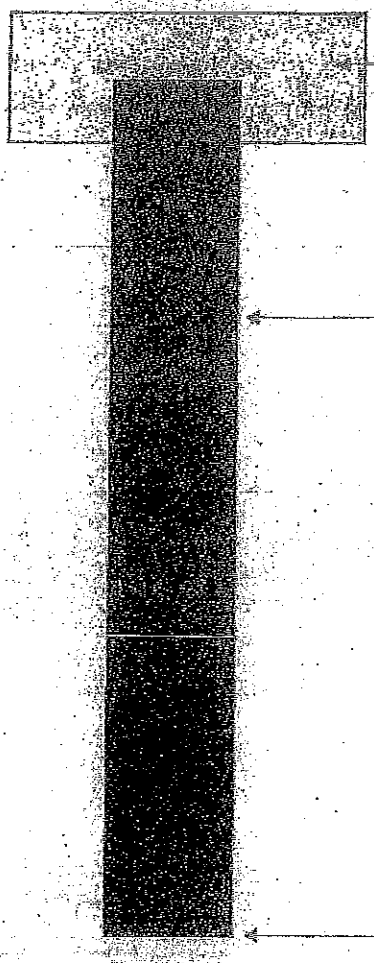
Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.945626
Longitude (Example: -120.12345) -122.950555
(WGS 84 Coordinate System)

Borehole diameter ____ inches Casing diameter 2" inches
Static water level ____ ft below top of casing Date ____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing ____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature
License No. 3269
Company Name Holt Services Inc

If trainee box is checked, sponsor's license number:
Sponsor's signature

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0 - 1 FT	0 - FT
	BACKFILL 1 - 16' FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 16' FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Type of Work:

☐ Construction
☑ Decommission ⇒ Original NOI No. 206282

Ecology Well ID Tag No. ACW087
Site Well Name SW-12
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for?

Notice of Intent No. AE91507

Type of Well:

☑ Resource Protection Well ☐ Injection Point
☐ Remediation Well ☐ Grounding Well
☐ Geotechnical Soil Boring ☐ Ground Source Heat Pump
☐ Environmental Boring ☐ Other
↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.945664
Longitude (Example: -120.12345) -122.950586
(WGS 84 Coordinate System)

Borehole diameter ____ inches Casing diameter 2" inches
Static water level ____ ft below top of casing Date ____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing ____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature
License No. 3269
Company Name Holt Services Inc

If trainee box is checked, sponsor's license number:
Sponsor's signature

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-15' FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 15' FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Type of Work:

☐ Construction
☑ Decommission ⇒ Original NOI No. 2039931

Ecology Well ID Tag No. AEM471
Site Well Name SW-13
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for?

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature
License No. 3269
Company Name Holt Services Inc

If trainee box is checked, sponsor's license number:
Sponsor's signature

Notice of Intent No. AE91507

Type of Well:

☑ Resource Protection Well ☐ Injection Point
☐ Remediation Well ☐ Grounding Well
☐ Geotechnical Soil Boring ☐ Ground Source Heat Pump
☐ Environmental Boring ☐ Other
↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.945966
Longitude (Example: -120.12345) -122.950802
(WGS 84 Coordinate System)

Borehole diameter ____ inches Casing diameter 2" inches
Static water level ____ ft below top of casing Date ____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing ____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-20 FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 20' FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Notice of Intent No. AE91507

Type of Work:

☐ Construction
☑ Decommission ⇨ Original NOI No. 20399 31

Ecology Well ID Tag No. AEM 478

Site Well Name SW-14

Consulting Firm LANDAU / DNR

Was a variance approved for this well/boring? ☐ Yes ☐ No

If yes, what was the variance for? _____

Type of Well:

☑ Resource Protection Well ☐ Injection Point
☐ Remediation Well ☐ Grounding Well
☐ Geotechnical Soil Boring ☐ Ground Source Heat Pump
☐ Environmental Boring ☐ Other _____
↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Property Owner WA State DNR

Well Street Address 9805 Blomberg St

City Tumwater County Thurston

Tax Parcel No. 12720130000

Location (see instructions): WWM ☐ or EWM ☐

SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W

Latitude (Example: 47.12345) 46.945524

Longitude (Example: -120.12345) -122.950767

(WGS 84 Coordinate System)

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer

Name (Print Last, First Name) Henderson, Cody

Driller/Engineer/Trainee Signature Cody H

License No. 3269

Company Name Holt Services Inc

If trainee box is checked, sponsor's license number: _____

Sponsor's signature _____

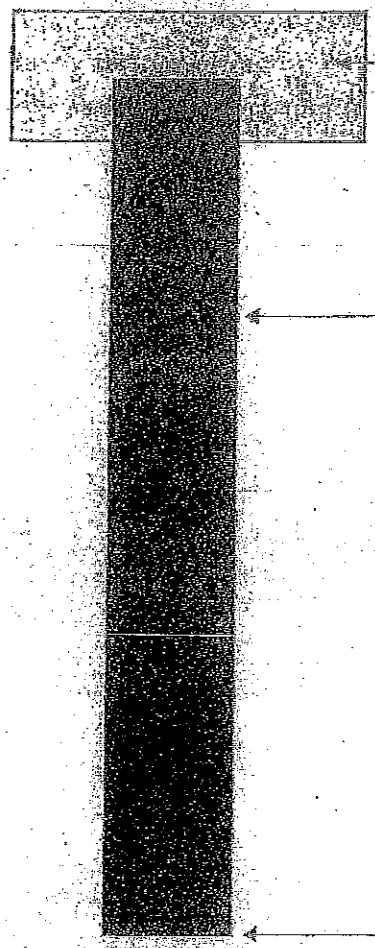
Borehole diameter _____ inches Casing diameter 2" inches

Static water level _____ ft below top of casing Date _____

☐ Above-ground completion with bollards ☐ Flush monument

↳ Stick-up of top of well casing _____ ft above ground surface

Start Date 3/18/2026 Completed Date 3/18/2026

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-20 FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 20' FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Notice of Intent No. AE91507

Type of Work:

☐ Construction
☑ Decommission ⇒ Original NOI No. 20239931

Type of Well:

☑ Resource Protection Well ☐ Injection Point
☐ Remediation Well ☐ Grounding Well
☐ Geotechnical Soil Boring ☐ Ground Source Heat Pump
☐ Environmental Boring ☐ Other
↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Ecology Well ID Tag No. AEM473
Site Well Name SW-15
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for?

Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

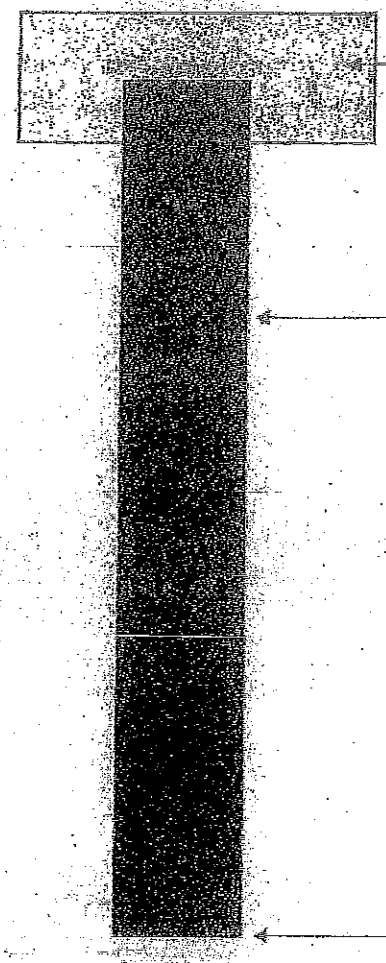
Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.945916
Longitude (Example: -120.12345) -122.950433
(WGS 84 Coordinate System)

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature
License No. 3269
Company Name Holt Services Inc

If trainee box is checked, sponsor's license number:
Sponsor's signature

Borehole diameter ____ inches Casing diameter 2" inches
Static water level ____ ft below top of casing Date ____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing ____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-20 FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 20 FT	

DEPARTMENT OF ECOLOGY
State of Washington

Resource Protection Well Report

Submit one well report per well installed. See page two for instructions.

Notice of Intent No. AE91507

Type of Work:
- ☐ Construction
- ☑ Decommission ⇒ Original NOI No. RQ39931

Type of Well:
- ☑ Resource Protection Well
- ☐ Remediation Well
- ☐ Geotechnical Soil Boring
- ☐ Environmental Boring
- ☐ Injection Point
- ☐ Grounding Well
- ☐ Ground Source Heat Pump
- ☐ Other
- ↳ ☐ Soil- ☐ Vapor- ☐ Water-sampling

Ecology Well ID Tag No. AEM474
Site Well Name SW-16
Consulting Firm LANDAU / DNR
Was a variance approved for this well/boring? ☐ Yes ☐ No
If yes, what was the variance for?

Property Owner WA State DNR
Well Street Address 9805 Blomberg St
City Tumwater County Thurston
Tax Parcel No. 12720130000

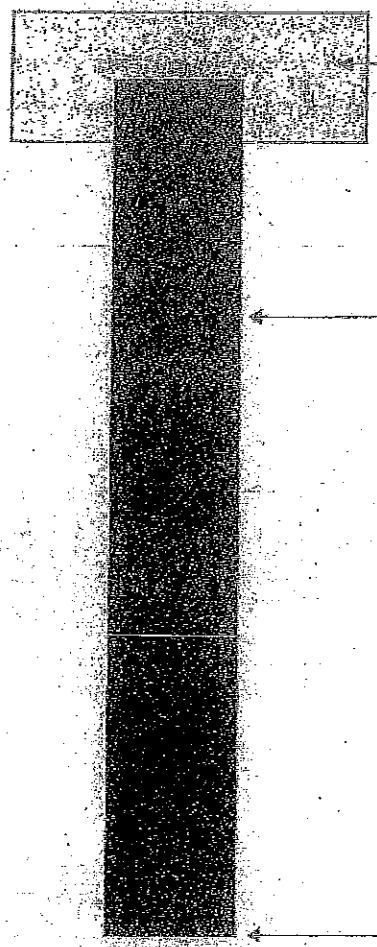
Location (see instructions): WWM ☐ or EWM ☐
SE ¼-¼ NE ¼, Section 20 Town 17N Range 2W
Latitude (Example: 47.12345) 46.945502
Longitude (Example: -120.12345) -122.950369
(WGS 84 Coordinate System)

WELL CONSTRUCTION CERTIFICATION: I constructed and/or accept responsibility for construction of this well, and its compliance with all Washington well construction standards. Materials used and the information reported are true to my best knowledge and belief.

☑ Driller ☐ Trainee ☐ Engineer
Name (Print Last, First Name) Henderson, Cody
Driller/Engineer/Trainee Signature
License No. 3269
Company Name Holt Services Inc

If trainee box is checked, sponsor's license number:
Sponsor's signature

Borehole diameter ____ inches Casing diameter 2" inches
Static water level ____ ft below top of casing Date ____
☐ Above-ground completion with bollards ☐ Flush monument
↳ Stick-up of top of well casing ____ ft above ground surface
Start Date 3/18/2026 Completed Date 3/18/2026

Construction/Design	Well Data	Formation Description
	CONCRETE SURFACE SEAL 0-1 FT	0 - FT
	BACKFILL 1-20 FT 3/8" Bentonite Chips	0 - FT
		0 - FT
	DEPTH OF BORING 20 FT	
