


# Port Angeles Rayonier Mill Timeline - 2010 Agreed Order to Plan for Interim Actions



Key	Volume I - Upland Data Summary Report	Volume III - Interim Action Alternatives Evaluation Report
	Volume II - Marine Data Summary Report	Volume IV - Draft Interim Action Plan

Schedule (Days = Calendar Days)	Deliverable	Vol.	Task
Within 30 days of effective date of Order	Table of Contents—Marine Data Summary Report	II	3a
Within 45 days of effective date of Order	Agency Review Draft Work Plan - Supplemental Upland Data Collection	I	1a
Within 60 days of receiving Ecology's comments on the Agency Review Draft Work Plan—Supplemental Upland Data Collection	Draft Final Work Plan—Supplemental Upland Data Collection	I	1b
As detailed in the Final Work Plan—Supplemental Upland Data Collection	Implement Final Work Plan—Supplemental Upland Data Collection	I	1c
Within 90 days of receiving Ecology's Port Angeles Harbor Sediment Characterization Study	Agency Review Draft—Marine Data Summary Report	II	3b
When the Agency Review Draft—Marine Data Summary Report is submitted	Marine data to Ecology's Environmental Information Management system	II	3c
Within 60 days of receiving validated data from the lab	Draft Supplemental Upland Data Collection Technical Memo	I	1d
When the Draft Supplemental Upland Data Collection Technical Memo is submitted	Table of Contents for the Upland Data Summary Report	I	2a
Within 75 days of receiving Ecology's comments on the Agency Review Draft—Marine Data Summary Report	Public Review Draft—Marine Data Summary Report	II	3d
Within 45 days of submittal of the Draft Supplemental Upland Data Collection Technical Memo and Agency Review Draft—Marine Data Summary Report	Draft Preliminary Cleanup Standards Section	III	4a
Within 105 days of receiving Ecology's comments of the Draft Supplemental Upland Data Collection Technical Memo	Agency Review Draft—Upland Data Summary Report	I	2b
When the Agency Review Draft—Upland Data Summary Report is submitted	Upland data to Ecology Environmental Information Management system	I	2c
Within 75 days of receiving Ecology's comments on the Agency Review Draft—Upland Data Summary Report	Public Review Draft—Upland Data Summary Report	I	2d
Within 120 days of submittal of both the Public Review Draft—Upland and Marine Data Summary Reports	Draft Preliminary Development of Interim Action Alternatives Section	III	4b
Within 105 days of receiving Ecology's comments on the Draft Preliminary Cleanup Standards and Development of Alternatives Sections	Agency Review Draft Interim Action Alternatives Evaluation Report	III	4c
Within 75 days of receiving Ecology's comments on the Agency Review Draft—Interim Action Alternatives Report	Public Review Draft Interim Action Alternatives Evaluation Report	III	4d
<b>Public Comment Period</b>			
Within 75 days of receiving Ecology revisions for the Public Review Draft of Upland Data Summary Report	Draft Final Upland Data Summary Report	I	2e
Within 75 days of receiving Ecology revisions for the Public Review Draft of Marine Data Summary Report	Draft Final Marine Data Summary Report	II	3e
Within 75 days of receiving Ecology revisions for the Public Review Draft of Interim Action Alternatives Evaluation Report	Draft Final Interim Action Alternatives Evaluation Report	III	4e
Within 60 days of Ecology approval of Volumes I, II, and III	Agency Review Draft Interim Action Plan	IV	5

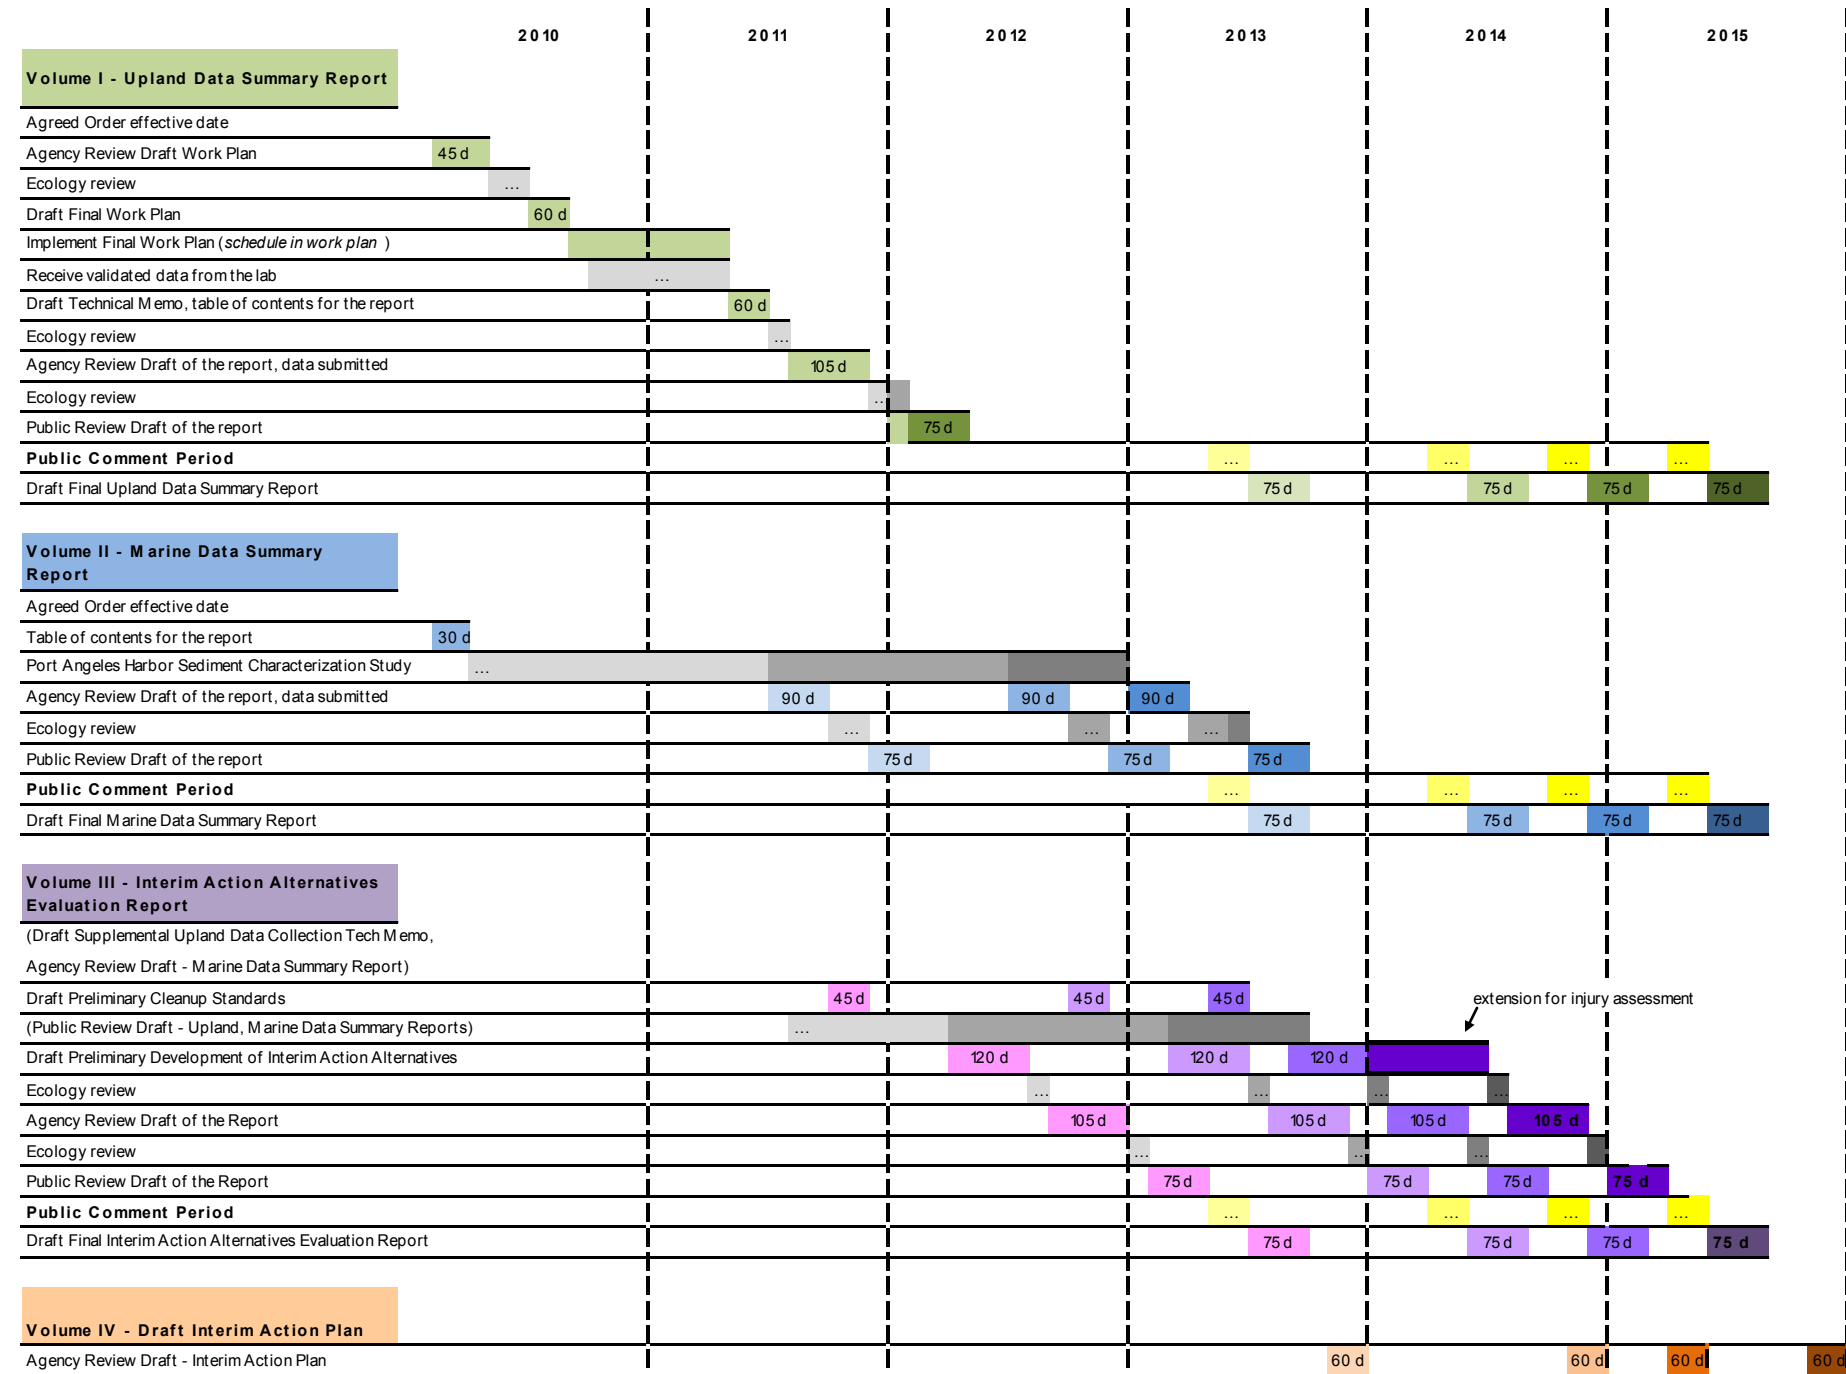

Timeline begins March 2010, after the public comment period for the Agreed Order, and ends middle of 2015. Volume IV is the final task under this Agreed Order.

... = review period (Ecology or lab)

... = public comment period

Darker colors show a shift from the previous, 2011 version of the timeline. The overall shift in schedule is due to a major delay in finalizing the Port Angeles Harbor Sediments Investigation Report. The January 2014 shift is for an extension of the due date of Rayonier's draft Interim Action Alternatives Section. This is to allow Rayonier to better study cleanup options that include restoration.
