ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		Contract Award	1 day	Mon 1/26/15	Mon 1/26/15	
2		Permitting	19 days	Tue 1/27/15	Fri 2/20/15	
3		Pre-Construction Meeting	1 day	Wed 2/18/15	Wed 2/18/15	
4		NTP	1 day	Fri 2/20/15	Fri 2/20/15	
5		Mobilization	1 day	Mon 2/23/15	Mon 2/23/15	4
6		Clean out Retail Store	4 days	Tue 2/24/15	Fri 2/27/15	5
7		HBM Abatement and Decom Wells	5 days	Mon 3/2/15	Fri 3/6/15	6
8		Demo Structure	5 days	Mon 3/9/15	Fri 3/13/15	7
9		Remove Overburden	5 days	Mon 3/16/15	Fri 3/20/15	8
10		Remove and Haul PCS	7 days	Mon 3/23/15	Tue 3/31/15	9
11		Install Infiltration Gallery	1 day	Wed 4/1/15	Wed 4/1/15	10
12		Backfill and Compact	5 days	Thu 4/2/15	Wed 4/8/15	11
13		Pave	1 day	Thu 4/9/15	Thu 4/9/15	12
14		As-Built Survey	1 day	Thu 4/9/15	Thu 4/9/15	13
15		Demobilize	1 day	Fri 4/10/15	Fri 4/10/15	14

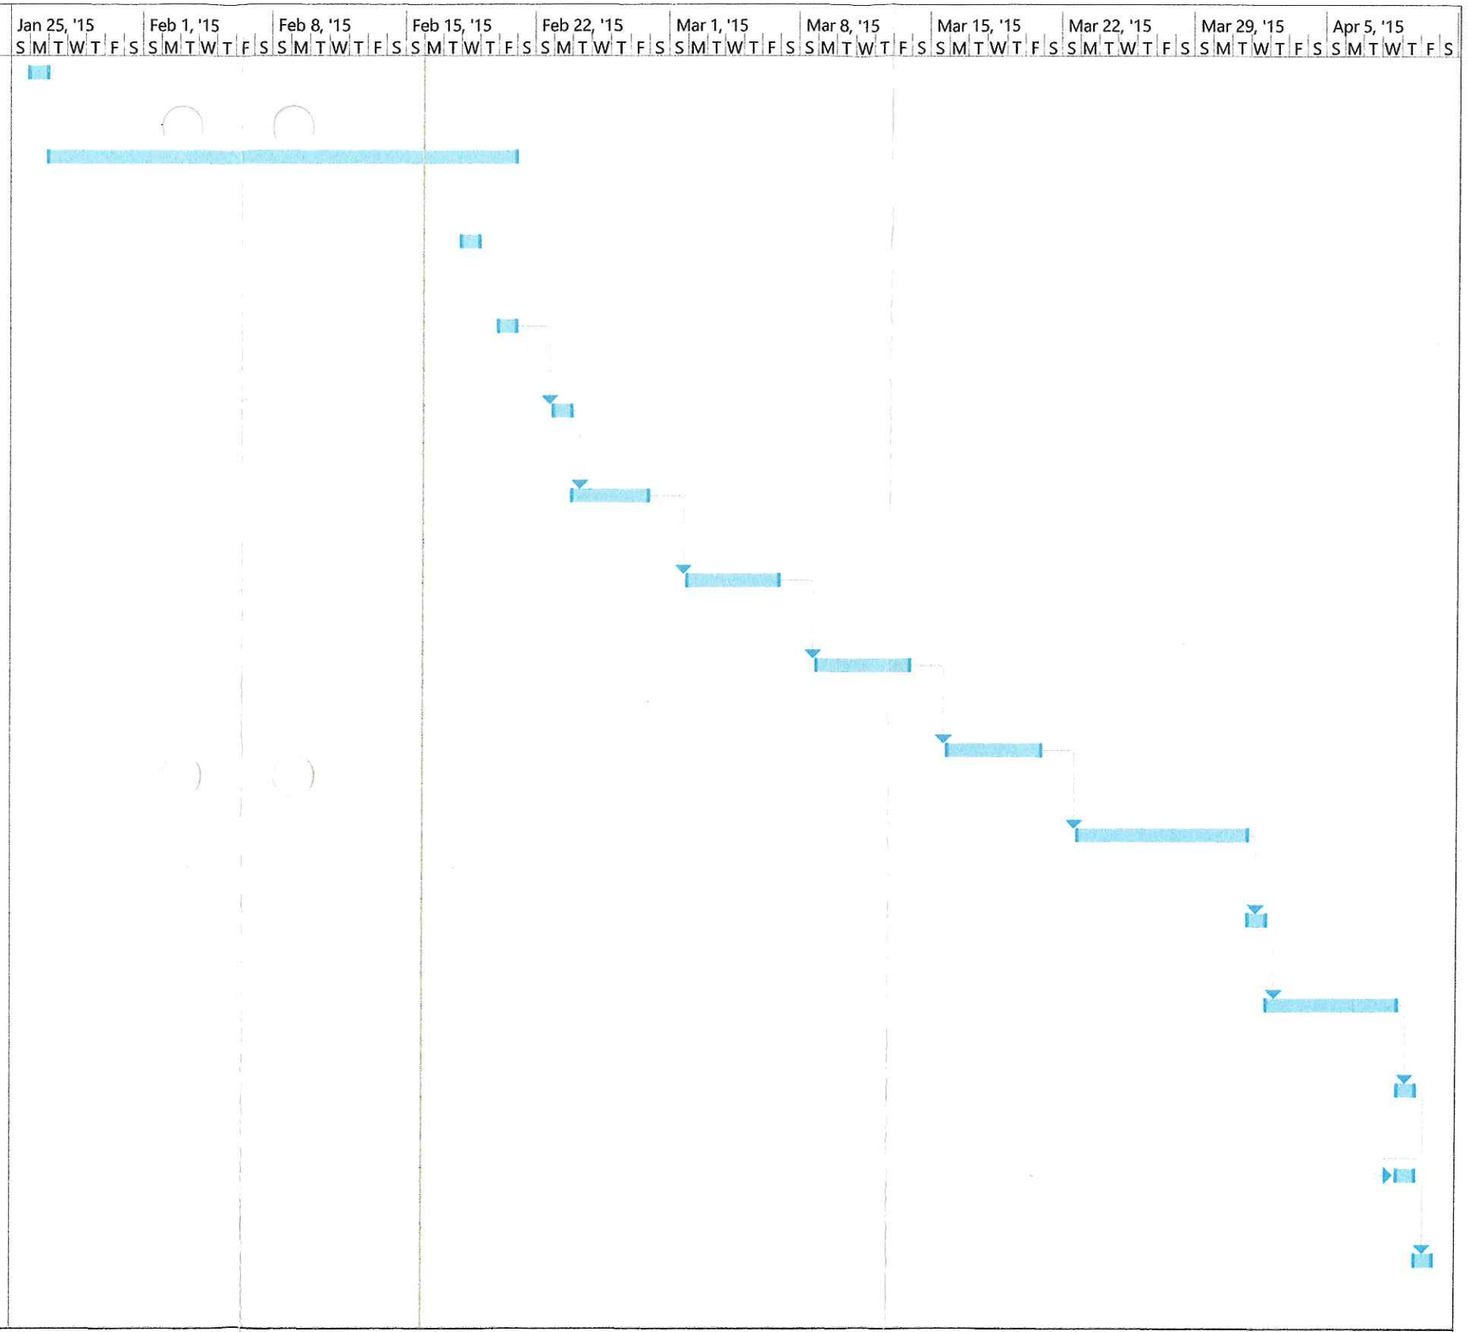

Project: Remedial Action Sched
Date: Mon 2/16/15

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual S ary Rollu	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		
